

I-SEM Cutover Run Sheet

Week 3

September 15th – 21st

Version 2.0

Introduction and Purpose

This document sets out the activities to be performed by Market Participants for the Week 3 of the I-SEM deployment cutover.

Participants are advised that the SEMOpX Auctions are not being conducted in the Market Trial environment from the 1st of September. SEMOpX production systems are available with credentials issued on the 11th of September, and trade gates opened on 12th of September.

The Balancing Market and SEMO Settlement will be conducted through September 2018 on a reasonable endeavours basis to facilitate deployment cutover and a smooth launch of I-SEM on 1st of October 2018. Participants may enter transactions in the Balancing Market and download reports if available, on the understanding that these reports will be published on a reasonable endeavours basis. Participants should note that internal cutover activities will take precedence during September 2018.

Gate opening for the Balancing Market was successfully completed on September 12th.

The run sheet is formatted as follows:

Time:	This defines the time period during which the activity is due to take place. Where a specific time is shown this indicates the latest time for the activity
Participants:	This will detail the 'Actors' that should participate in the Activity, where this is not set to 'All' it will highlight the specific 'Actors' as defined in the Market Participant Guide
Activity:	This details the activity that the participants should perform during this time period
Inputs:	This details all of the inputs required for the defined activity
Outputs:	This details all outputs from the defined activity

Technical Cutover for SEMOpX

Participants may commence the preparation of their systems for the SEMOpX cutover. See [Participant cutover guide Section 3 SEMOpX Markets](#). All SEMOpX Queries should be managed through the production support arrangements. Production credentials for ETS, M7 and SMSS were issued to Participants on **September 11th**. These credentials allow, Participants to interact with the SEMOpX production systems as follows:

ETS:

- Test connectivity to ETS (from 11th of September onwards).
- Submit orders to ETS (from 12th of September onwards) for the Ex-Ante Auctions (DAM/IDA1/IDA2/IDA3 for the 1st of October)

M7:

- Test connectivity to M7 11th (from 11th of September onwards).
- Participants cannot submit orders to M7 until the gate opens for Intraday Continuous Trading on the 30th of September.

SMSS:

- Log into the SMSS portal and test connectivity to the Secure File Transfer Protocol (SFTP) server (from 11th of September onwards).
- Reports will be available after go-live on 1 October 2018.

Technical Cutover for SEMO Balancing Market

The Balancing Market Interface (BMI) used for Market Trial has transitioned to production system. The gate opening for bidding on October 1st, successfully opened as planned on September 12th.

EDIL cutover is scheduled on September 30th, provisionally between 7am and 11am. Details of the EDIL cutover sequence will be published in Cutover run sheet 4 (September 22nd -28th). Participants are reminded that there is a java upgrade required for the EDIL cutover.

The Public Website was deployed on September 12th.. The url change for the website will occur on September 27th.

Standing Commercial Offer Data

Newly entered and updates to standing Commercial Offer Data will take 19 days prior to the trading day to become effective within the Balancing Market System.

Letters of Credit (LOC)/Deposits to Cash Collateral Account

Participants should submit any new LOC or deposits to the Cash Collateral Accounts by 10th of September for Market Operator approval by 17th of September.


Data

Balancing Market interface remains open this week. There are no obligations on participants to submit trial data during the cutover period. Participants may submit data such as physical notifications, updated default COD, if they so wish. Gate opening (D-19) for the Balancing Market and Day Ahead Market opened on **September 12th**.

Meter Data (Trade day+1 & Trade day+4) will be submitted daily in accordance with the run sheet by all Meter Data Providers.

SEMOpX **Production** Environment for ETS / M7 remains open this week, with interactions as outlined above.

I-SEM Deployment Timeline

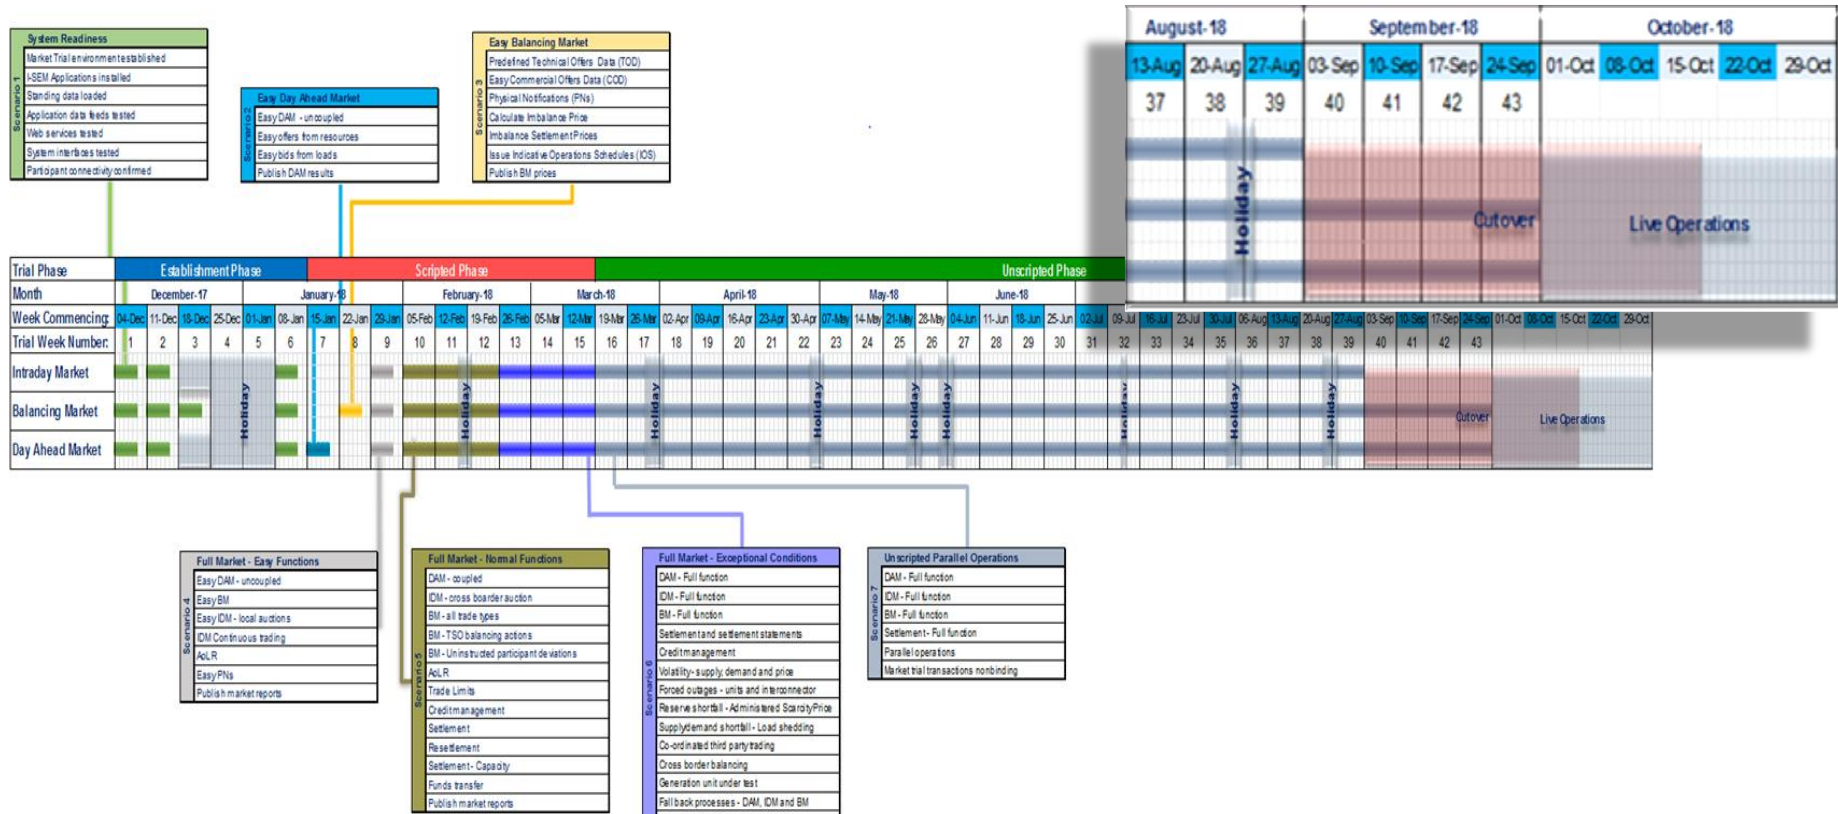

Day 1: Saturday 15th September

Day 1 - Saturday 15 th of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours

Day 2: Sunday 16th September

Day 2 - Sunday 16 th of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours

Day 3: Monday 17th of September

Day 3 – Monday 17th of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
09:30 - 10:00	All	Conference Call	Team provide briefing of the day's activities and ensure that run sheet is available to all participants	Participant inquiries and clarifications on events for the day
14:00	MDP's	Submissions of D+1 Meter Data	1. D+1 Meter data files provided from external MDP's 2. D+1 Meter data files provided from internal MDP's	Successful submission of D+1 Meter Data
14:00	MDP's	Submissions of D+4 Meter Data	1. D+4 Meter data files provided from external MDP's 2. D+4 Meter data files provided from internal MDP's	Successful submission of D+4 Meter Data
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours
16:00	All	Settlement Run is executed – reasonable endeavours	EirGrid scripted data	Settlement Reports – reasonable endeavours
16:30 - 17:00	All	Conference Call	Highlight any issues / concerns: Team provides update on any issues and issue Run Sheets for next day	Market Participant Survey

Day 4: Tuesday 18th of September

Day 4 – Tuesday 18th of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
09:30 - 10:00	All	Conference Call	Team provide briefing of the day's activities and ensure that run sheet is available to all participants	Participant inquiries and clarifications on events for the day
14:00	MDP's	Submissions of D+1 Meter Data	1. D+1 Meter data files provided from external MDP's 2. D+1 Meter data files provided from internal MDP's	Successful submission of D+1 Meter Data
14:00	MDP's	Submissions of D+4 Meter Data	1. D+4 Meter data files provided from external MDP's 2. D+4 Meter data files provided from internal MDP's	Successful submission of D+4 Meter Data
15:00	All	Dispatch Cutover Q&A Session 15:00 – 16:00.	N/A	N/A
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours
16:00	All	Settlement Run is executed – reasonable endeavours	EirGrid scripted data	Settlement Reports – reasonable endeavours

16:30 - 17:00 All

Conference Call

Highlight any issues / concerns:
Team provides update on any issues and
issue Run Sheets for next day

Market Participant Survey

Day 5: Wednesday 19th of September

Day 5 – Wednesday 19th of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
09:30 - 10:00	All	Conference Call	Team provide briefing of the day's activities and ensure that run sheet is available to all participants	Participant inquiries and clarifications on events for the day
14:00	MDP's	Submissions of D+1 Meter Data	1. D+1 Meter data files provided from external MDP's 2. D+1 Meter data files provided from internal MDP's	Successful submission of D+1 Meter Data
14:00	MDP's	Submissions of D+4 Meter Data	1. D+4 Meter data files provided from external MDP's 2. D+4 Meter data files provided from internal MDP's	Successful submission of D+4 Meter Data
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours
16:00	All	Settlement Run is executed – reasonable endeavours	EirGrid scripted data	Settlement Reports – reasonable endeavours
16:30 - 17:00	All	Conference Call	Highlight any issues / concerns: Team provides update on any issues and issue Run Sheets for next day	Market Participant Survey

Day 6: Thursday 20th of September

Day 6 – Thursday 20 st of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
09:30 - 10:00	All	Conference Call	Team provide briefing of the day's activities and ensure that run sheet is available to all participants	Participant inquiries and clarifications on events for the day
14:00	MDP's	Submissions of D+1 Meter Data	1. D+1 Meter data files provided from external MDP's 2. D+1 Meter data files provided from internal MDP's	Successful submission of D+1 Meter Data
14:00	MDP's	Submissions of D+4 Meter Data	1. D+4 Meter data files provided from external MDP's 2. D+4 Meter data files provided from internal MDP's	Successful submission of D+4 Meter Data
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours
16:00	All	Settlement Run is executed – reasonable endeavours	EirGrid scripted data	Settlement Reports – reasonable endeavours
16:30 - 17:00	All	Conference Call	Highlight any issues / concerns: Team provides update on any issues and issue Run Sheets for next day	Market Participant Survey

Day 7: Friday 21st of September

Day 7 – Friday 21 st of September 2018				
Time	Participants	Activity	Inputs	Outputs
All Day	D-Gen O-Gen AU Sup DSU	Ex-ante – Data Submissions Production ETS and M7 systems are available. The Market Trial ETS and M7 systems are no longer available for submissions.	Commercial Offer Data submitted by Participants	No outputs – No auctions will be conducted
09:30 - 10:00	All	Conference Call	Team provide briefing of the day's activities and ensure that run sheet is available to all participants	Participant inquiries and clarifications on events for the day
14:00	MDP's	Submissions of D+1 Meter Data	1. D+1 Meter data files provided from external MDP's 2. D+1 Meter data files provided from internal MDP's	Successful submission of D+1 Meter Data
14:00	MDP's	Submissions of D+4 Meter Data	1. D+4 Meter data files provided from external MDP's 2. D+4 Meter data files provided from internal MDP's	Successful submission of D+4 Meter Data
16:00	All	BM – Market Results Available Participants may connect to the Balancing Market Interface and download available reports – reasonable endeavours	Balancing Market Run completed and specified reports are available	BM Reports are downloaded – reasonable endeavours
16:00	All	Settlement Run is executed – reasonable endeavours	EirGrid scripted data	Settlement Reports – reasonable endeavours
16:30 - 17:00	All	Conference Call	Highlight any issues / concerns: Team provides update on any issues and issue Run Sheets for next day	Market Participant Survey
